

**DEPARTMENT OF PUBLIC WORKS**

*Michael Fraser, Director of Public Works  
Karlton Place, P.E., City Engineer*

300 West Ash · P.O. Box 736  
Salina, Kansas 67402-0736



TELEPHONE · (785) 309-5725

FAX · (785) 309-5713

TDD · (785) 309-5747

E-MAIL · [mike.fraser@salina.org](mailto:mike.fraser@salina.org)

[karlton.place@salina.org](mailto:karlton.place@salina.org)

WEBSITE · [www.salina-ks.gov](http://www.salina-ks.gov)

**CITY OF SALINA  
CONSTRUCTION PROJECT UPDATE  
2006-2007 CAPITAL IMPROVEMENTS PROGRAM  
SEPTEMBER, 2007**

PROJECT NO. 00-1248

**NORTH OHIO STREET GRADE SEPARATION**

CONTRACTOR: King Construction  
Hesston, KS

ORIGINAL CONTRACT AMOUNT: \$20,300,000.00

**SCOPE OF PROJECT:** This project involves the construction of a 600-foot-long overpass bridge across the railroad lines on North Ohio Street between York Street and Pacific Avenue.

**STATUS OF PROJECT:** The majority of work on this project is complete. Items to be complete include the installation of path way lighting poles. Landscaping will involve, seeding, trees and flower plantings which will put the finishing touches on the project.



PROJECT NO. 07-2625

**2007 ADA RAMPS**

CONTRACT COMPLETION DATE: November 2007

ORIGINAL AMOUNT: \$100,000

**SCOPE OF PROJECT:** This project involves the installation of handicap ramps at various locations through out the City.

**STATUS OF PROJECT:** At this time more than 50% of the locations have been completed for this year's project.



Engineering ♦ Streets ♦ Flood Control ♦ Traffic Control  
Central Garage ♦ Sanitation ♦ Landfill ♦

Our Mission is to Build and Maintain a Clean, Safe Community

PROJECT NO. 06-1586

**SPRING AND FALL STREET MARKING**

CONTRACTOR: Twin Traffic Inc., Kansas City  
CONTRACT APPROVAL DATE: April 25, 2006  
CONTRACT COMPLETION DATE: November 15, 2007  
ORIGINAL CONTRACT AMOUNT: \$26,000.00



**SCOPE OF PROJECT:** This project provides for the street pavement marking to be applied once in the spring and again in the fall for the years 2006 and 2007. Over 53 miles of streets are painted with white or yellow centerline or edge line markings each season.

**STATUS OF PROJECT:** Spring pavement marking is completed and Fall marking will begin this Fall.

PROJECT NO. 06-1612

**GOLDEN EAGLE PHASE III**

CONTRACTOR: APAC-KS/Shears, Salina  
CONTRACT APPROVAL DATE:  
ORIGINAL AMOUNT: \$352,934.30



**SCOPE OF PROJECT:** This project consists of curb, gutter, pavement, grading and drainage for approximately 1,124 lineal feet of Red Hawk Lane and 125 lineal feet of Wayne Avenue, installation of approximately 517 lineal feet of storm sewer and inlets, approximately 1,233 lineal feet of 6" and 8" water main, fire hydrants and approximately 1,214 lineal feet of 8" and 10" sanitary sewer main and manholes.

**STATUS OF PROJECT:** Water, sewer and storm sewer lines have been installed. The next phase of this project will be dirt grading in preparation for construction of curb and gutter and asphalt pavement.

PROJECT NO. 07-2645

**QUAIL MEADOWS – PHASE III SUBDIVISION IMPROVEMENTS**

CONTRACTOR: APAC-KS/Shears, Salina  
CONTRACT APPROVAL DATE:  
ORIGINAL CONTRACT AMOUNT: \$234,126.20



**SCOPE OF PROJECT:** This project involves the third phase of construction of waterline, sanitary sewer, storm sewer, concrete curb and gutter and asphalt streets. Quail Meadows Addition is located at the north west corner of Schilling Road and South Ohio Street. Additions to the City's infrastructure include 930 feet of water line, 1,280 feet of sewer line, and 506 feet of storm pipeline and 2,810 square yards of asphalt pavement.

**STATUS OF PROJECT:** Work on this project has been completed and building permits have been issued.

PROJECT NO. 06-1607

**LIBERTY ADDITION PHASE II**

CONTRACTOR: APAC-KS/Shears, Salina  
CONTRACT APPROVAL DATE:  
ORIGINAL CONTRACT AMOUNT: \$612,454.55



**SCOPE OF PROJECT:** This project consists of curb, gutter, pavement, grading and drainage for approximately 2,352 lineal feet of Cortland Circle as well as the installation of approximately 879 lineal feet of storm sewer and manholes, approximately 2,906 lineal feet of 6" and 8" water main and fire hydrants, 1,844 lineal feet of sanitary sewer main, manholes, and the construction of a reinforced concrete box culvert.

**STATUS OF PROJECT:** This project has been completed.

PROJECT NO. 07-2645

**2007 CURB & GUTTER AND CONCRETE PAVEMENT IMPROVEMENTS**

CONTRACTOR: PAVER'S, INC.  
CONTRACT APPROVAL DATE:  
ORIGINAL CONTRACT AMOUNT: \$176,600.00



**SCOPE OF PROJECT:** This project is part of the City's annual street maintenance program. It involves repairs to existing concrete streets located on Riverside Drive, Wesley Street, Minneapolis Ave., McAdams Road, Park Street and Spruce Street.

**STATUS OF PROJECT:** Work on this project is expected to begin in late October.

PROJECT NO.07-1623

**2007 STREET IMPROVEMENT SLURRY SEAL**

CONTRACTOR: Ballou Construction  
CONTRACT APPROVAL DATE:  
ORIGINAL CONTRACT AMOUNT: \$204,317.50


**SCOPE OF PROJECT:** Latex Modified Slurry Seal involves the application of mixture of Fine Aggregate, Asphalt Emulsion, and Portland Cement, to preserve the existing surface of the roadway.

**STATUS OF PROJECT:** Work is scheduled to begin this fall and is expected to be completed within a few weeks from the time that it starts.

PROJECT NO. 03-1409

**NORTH BROADWAY BOULEVARD CORRIDOR IMPROVEMENTS**

CONTRACTOR: Pavers Inc.  
CONTRACT APPROVAL DATE:  
ORIGINAL CONTRACT AMOUNT: \$2,148,949.00

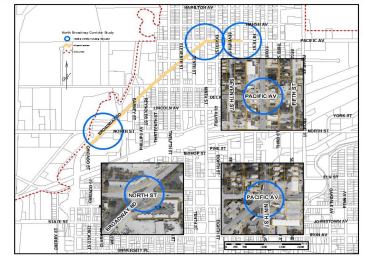

**SCOPE OF PROJECT:** This project involves the rehabilitation of North Broadway Boulevard from North Street to Ninth Street and Pacific Avenue from Ninth Street to Santa Fe Avenue. The pavement will be milled/overlaid with asphalt, four lanes will be converted to three lanes, intersections will be realigned, new traffic signals will be installed and curb/gutter will be reconstructed.

**STATUS OF PROJECT:** Reconstruction of new curb & gutter and realignment of intersections is completed on the north half of the project. Work is being preformed on the south half of the project to reconstruct curb & gutter and realign intersections. Milling and new asphalt should be taking place very soon on Broadway Boulevard itself.

PROJECT NO. 05-1547

**DOWNTOWN TRAFFIC SIGNAL IMPROVEMENTS**

CONTRACTOR: Kayton Electric  
CONTRACT APPROVAL DATE:  
ORIGINAL CONTRACT AMOUNT: \$692,042.26



**SCOPE OF PROJECT:** This project involves the redesign of four existing downtown traffic signal systems located at Santa Fe and Iron, Santa Fe and Walnut, 5th and Iron and 7th and Iron.

**STATUS OF PROJECT:** All locations have been completed with the exception of 7th and Iron which is under construction at present time.



PROJECT NO. 07-1621

**2007 ASPHALT ARTERIAL MAJOR MAINTENANCE**

CONTRACTOR: APAC-KS/Shears, Salina  
CONTRACT APPROVAL DATE:  
ORIGINAL CONTRACT AMOUNT: \$1,040,046.88  
ORIGINAL CONTRACT AMOUNT:



**SCOPE OF PROJECT:** This project consists of mill up of old asphalt and the placement of new asphalt. Locations included in this years project are Santa Fe, Iron Ave., Crawford Street and Broadway Blvd.

**STATUS OF PROJECT:** All locations are complete with the exception of a portion of Santa Fe still left to do as well as the section on Iron Street also remaining to be completed.

PROJECT NO. 07-2643

**MAGNOLIA HILLS SUBDIVISION IMPROVEMENT PHASE 2**

CONTRACTOR: APAC-KS/Shears, Salian  
CONTRACT APPROVAL DATE:  
ORIGINAL CONTRACT AMOUNT: \$474,510.55



**SCOPE OF PROJECT:** This project consists of curb, guttering, paving, grading and drainage for approximately 3,103 lineal feet of Brookfield Drive, Kaysn Lane, Sunset Ridge Drive, and Dunnwood Drive. The installation of approximately 294 lineal feet of storm drainage, approximately 1,836 lineal feet of six-inch water main, fire hydrants, approximately 1,326 lineal feet of sanitary sewer main and manholes.

**STATUS OF PROJECT:** Water, sewer and storm sewer lines have been installed. The next phase of this project will be dirt grading in preparation for construction of curb and gutter and asphalt pavement.

PROJECT NO: 07-1624  
**ARTERIAL SIDEWALKS**

CONTRACTOR: Davis Concrete Construction  
CONTRACT APPROVAL DATE:  
ORIGINAL CONTRACT AMOUNT: \$63,717.75



**SCOPE OF PROJECT:** This project includes the construction of concrete sidewalks along arterial streets and streets designated as school safe walking routes. Locations for this years project include Quincy Street, Wayne Avenue, Simmons Street, North Street and Hartland Avenue.

**STATUS OF PROJECT:** Approximately 25% of the work on this project is completed and is expected to be completed this fall.

PROJECT NO. 06-1603  
**RAILROAD CORSSING REMOVALS**

DESIGNER: City Staff  
CONTRACTOR: Lancaster, Construction  
ORIGINAL CONTRACT AMOUNT: \$104,046.88



**SCOPE OF PROJECT:** This project includes the removal eight (8) UPRR railroad crossings on existing city streets and replacement with new pavement. The City agreed to this obligation as part of the North Ohio Street overpass project which resulted in a total of 19 railroad crossing removals. The other 11 crossings were removed on Ohio Street as part of the project. The City is collaborating with K&O RR to allow them to meet their federally required financial obligation on this project using in-kind services.

**STATUS OF PROJECT:** This project has been completed and is now open to traffic.
